Manufacture :

Kalorindo
PT. INTAN PRIMA KALORINDO

Client :

PERTAMINA
PATRA NIAGA

PROJECT WEEKLY PROGRESS REPORT	Document Number : IPK/K26015/TB&CN/WPR-01 Date : : 21-Sep-26

WEEK ENDING NUMBER
6

PT. PERTAMINA PATRA NIAGA RU VI BALONGAN

PENGADAAN CHANNEL ASSY 38-E-110, 12-E-522A, 14-E-201A&B, 12-E-501B 12-E-522C & TUBE BUNDLE ASSY 16-E-120C, 16-E-108, 16-E-113, 16-E-114, 19-E-107, 20-E-109A, 20-E-109B

Contract No. : 4500074960

Rev	Date	Description	Prepared By.	Comp.
			Rama Danu F	
0	21-Sep-26	ISSUED FOR INFORMATION		

Manufacture :

KALORINDO
PT. INTAN PRIMA KALORINDO

WEEKLY PROGRESS REPORT

Pengadaan Channel Assy 38-E-110, 12-E-522A, 14-E-201A&B, 12-E-522C, 12-E-501B & Pengadaan Tube Bundle Assy 16-E-102C, 16-E-108, 16-E-113, 16-E-114, 19-E-107, 20-E-109A, 20-E-109B


Cut of Date 6 21-Sep-26

Client :


PERTAMINA PATRA NIAGA

Contract No.	:	4500074960
Project Name	:	Pengadaan Channel Assy 38-E-110, 12-E-522A, 14-E-201A&B, 12-E-522C, 12-E-501B & Pengad
Plant	:	PT. PERTAMINA PATRA NIAGA RU VI Balongan
Starts	:	10-Aug-26
Finish	:	19-Feb-27

Works Duration	:	193	days
Time Elapsed	:	43	days
Time Remaining	:	150	days



Progress Actual	:	15,51%
Progress Remaining	:	84,49%



MAJOR ISSUE, AREA OF CONCERN OR BOTTLENECKS

Description	Action Plan	Status

DOWN TIME

1) Operation	:	N/A
2) Weather	:	N/A
3) Contractor Issue	:	N/A
4) Force Majeure	:	N/A

MAJOR ACTIVITIES / ACCOMPLISHMENT - THIS PERIODE

DOKUMENT VDRL : Submit & Approval Document

PROCUREMENT : PO & Monitoring Material

FABRICATION : : -

TESTING : : -

DELIVERY : : -

MAJOR ACTIVITIES / OBJECTIVES - NEXT WEEK

DOKUMENT VDRL : Submit & Approval Document

PROCUREMENT : PO & Monitoring Material


FABRICATION : : -

TESTING : : -

DELIVERY : : -

WEIGHT ACHIEVEMENT

	ACTIVITIES	WEIGHT	PLANNED	ACTUAL	VARIANCE
1.	DOCUMENT VDRL	26,63%	62,66%	43,48%	-19,18%
2.	PROCUREMENT	37,60%	9,58%	10,44%	0,86%
3.	FABRICATION	32,64%	0,00%	0,00%	0,00%
4.	TESTING	0,52%	0,00%	0,00%	0,00%
5.	FINISHING & PACKAGING	2,09%	0,00%	0,00%	0,00%
6.	DELIVERY	0,52%	0,00%	0,00%	0,00%
	TOTAL PROGRESS	100,00%	20,29%	15,51%	-4,78%

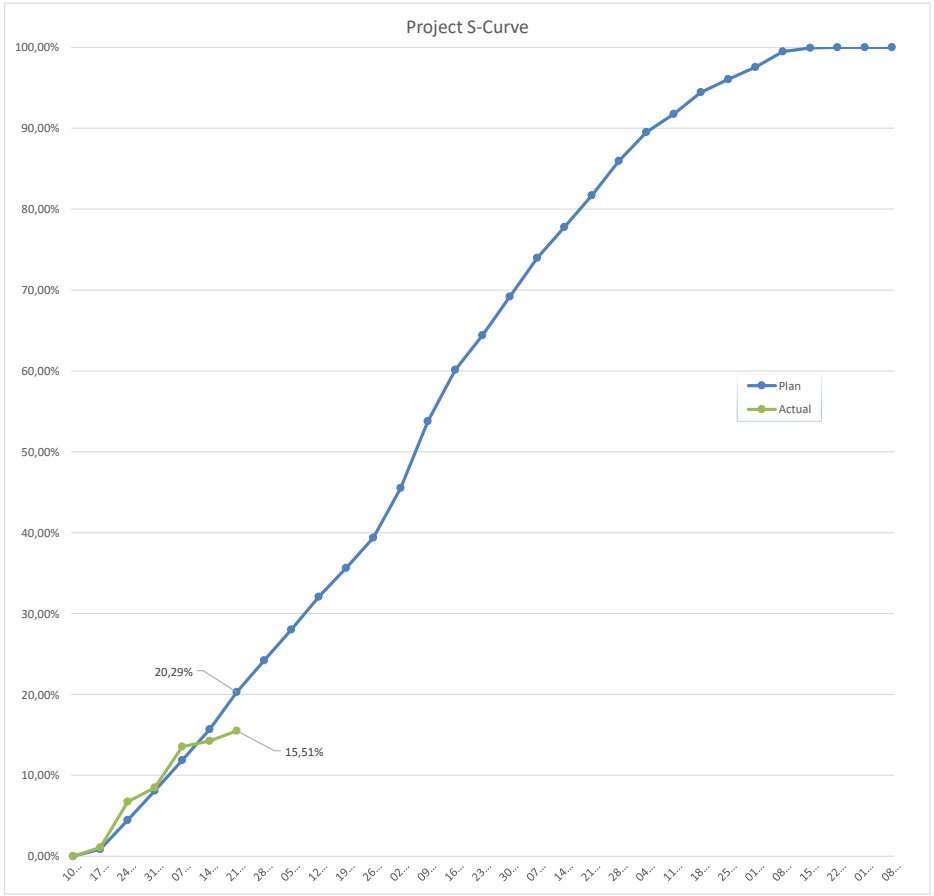

Manufacture :

KALORINDO
PT. INTAN PRIMA KALORINDO

End User :

PERTAMINA
PATRA NIAGA

PENGADAAN CHANNEL ASSY 38-E-110, 12-E-522A, 14-E-201A&B, 12-E-501B 12-E-522C & TUBE BUNDLE ASSY 16-E-120C, 16-E-108, 16-E-113, 16-E-114, 19-E-107, 20-E-109A, 20-E-109B

SUMMARY PROGRESS

Contract No.	:	4500074960	
Project Name	:	Pengadaan Channel Assy 38-E-110, 12-E-522A, 14-E-201A&B, 12-E-522C, 12-E-501B & Pengadaan Tube Bundle Assy 16-E-102C, 16-E-108, 16-E-113, 16-E-114, 19-E-107, 20-E-109A, 20-E-109B	
Plant	:	PT. PERTAMINA PATRA NIAGA RU VI Balongan	
Starts	:	10-Aug-26	
Finish	:	19-Feb-27	
Cut of Date	:	6	21-Sep-26
Revision No.	:	0	

NO.	Description	WF %	Physical Progress (%)							Remarks
			Plan			Actual			Variance	
			Previous	This Week	Cum.	Previous	This Week	Cum.		
		100,00%	15,66%	4,63%	20,29%	14,24%	1,26%	15,51%	-4,78%	
1	DOCUMENT VDRL	26,63%	48,80%	13,86%	62,66%	43,48%	0,00%	43,48%	-19,18%	
2	PROCUREMENT	37,60%	7,09%	2,49%	9,58%	7,09%	3,36%	10,44%	0,86%	
3	FABRICATION	32,64%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
4	TESTING	0,52%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
5	FINISHING & PACKAGING	2,09%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
6	DELIVERY	0,52%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	

Prepared by,
PT Intan Prima Kalorindo

Rama Danu Fahriza
Monday, 21 September 2026

Checked by,
PT Intan Prima Kalorindo

Hadi Ramdan
Monday, 21 September 2026

Approved by,
PT. PERTAMINA PATRA NIAGA RU IV CILACAP

Name :
Date :

PENGADAAN CHANNEL ASSY 38-E-110, 12-E-522A, 14-E-201A&B, 12-E-501B 12-E-522C & TUBE BUNDLE ASSY 16-E-120C, 16-E-108, 16-E-113, 16-E-114, 19-E-107, 20-E-109A, 20-E-109B

DOCUMENT VDRL

Manufacture : KALORINDO PT. INTAN PRIMA KALORINDO

End User : PERTAMINA PATRA NIAGA

Contract No.	:	4500074960
Project Name	:	Pengadaan Channel Assy 38-E-110, 12-E-522A, 14-E-201A&B, 12-E-522C, 12-E-501B & Pengadaan Tube Bundle Assy 16-E-102C, 16-E-108, 16-E-113, 16-E-114, 19-E-107, 20-E-109A, 20-E-109B
Plant	:	PT. PERTAMINA PATRA NIAGA RU VI Balongan
Cut of Date	:	6 21-Sep-26
Revision No.	:	0

No.	Description Item	Weight Factor (%)	Schedule Plan		Plan			Actual			Remarks
			Start	Finish	Last Week	This Week	Cumulative	Last Week	This Week	Cumulative	
1	DOCUMENT VDRL	26,63%	07-Nov-25	31-Dec-25	48,80%	13,86%	62,66%	43,48%	0,00%	43,48%	
1.1	Drawing Tube Bundle	10,00%	17-Aug-26	16-Sep-26	84,00%	16,00%	100,00%	84,00%	0,00%	84,00%	
1.2	Drawing Channel	10,00%	17-Aug-26	16-Sep-26	84,00%	16,00%	100,00%	100,00%	0,00%	100,00%	
1.3	ITP	10,00%	21-Aug-26	20-Sep-26	80,00%	20,00%	100,00%	70,00%	0,00%	70,00%	
1.4	Welding & NDE Map	16,00%	24-Aug-26	08-Oct-26	50,00%	13,00%	63,00%	0,00%	0,00%	0,00%	
1.5	Manufacture Procedure	22,00%	16-Sep-26	15-Nov-26	0,00%	11,00%	11,00%	24,00%	0,00%	24,00%	
1.6	Welder List & Certificates	16,00%	24-Aug-26	08-Oct-26	50,00%	13,00%	63,00%	40,00%	0,00%	40,00%	
1.7	WPS & PQR	16,00%	24-Aug-26	08-Oct-26	50,00%	13,00%	63,00%	40,00%	0,00%	40,00%	

Prepared by,
PT Intan Prima Kalorindo

Rama Danu Fahriza
Monday, 21 September 2026

Checked by,
PT Intan Prima Kalorindo

Hadi Ramdan
Monday, 21 September 2026

Approved by,
PT. PERTAMINA PATRA NIAGA RU IV CILACAP

Name :
Date :

Manufacture : Client :

PENGADAAN CHANNEL ASSY 38-E-110, 12-E-522A, 14-E-201A&B, 12-E-501B 12-E-522C & TUBE BUNDLE ASSY 16-E-120C, 16-E-108, 16-E-113, 16-E-114, 19-E-107, 20-E-109A, 20-E-109B

PROCUREMENT WORKS

Contract No. : 4500074960
Project Name : Pengadaan Channel Assy 38-E-110, 12-E-522A, 14-E-201A&B, 12-E-522C, 12-E-501B & Pengadaan Tube Bundle Assy 16-E-102C, 16-E-108, 16-E-113, 16-E-114, 19-E-107, 20-E-109A, 20-E-109B
Plant : PT. PERTAMINA PATRA NIAGA RU VI Balongan
Cut of Date : 6 21-Sep-26
Revision No. : 0

No.	Description Item	Weight Factor (%)	Schedule Plan		Plan			Actual			Remarks
			Start	Finish	Last Week	This Week	Cumulative	Last Week	This Week	Cumulative	
2	PROCUREMENT WORKS	37,60%	24-Nov-25	05-Feb-26	7,09%	2,49%	9,58%	7,09%	3,36%	10,44%	
2.1	MATERIAL FOR TUBE BUNDLE	60,00%	24-Nov-25	04-Mar-26	4,00%	2,98%	6,98%	4,00%	20,00%	24,00%	
2.1	Tubes, U Tubes SA 179 & Tube Spacer	25,00%	20-Aug-26	29-Jan-27	16,00%	4,00%	20,00%	16,00%	4,00%	20,00%	
2.2	Tubesheet SA 266	25,00%	20-Aug-26	29-Jan-27	16,00%	4,00%	20,00%	16,00%	4,00%	20,00%	
2.3	Plate SA 283 Gr.C for Baffle, Support Baffle, Impingement, Seal Bars, Skid Bars	7,00%	16-Sep-26	31-Oct-26	0,00%	14,00%	14,00%	0,00%	14,00%	14,00%	
2.4	Plate SA 516 Gr.70 for Baffle, Support Baffle, Impingement, Seal Bars, Skid Bars	3,00%	23-Sep-26	12-Oct-26	0,00%	0,00%	0,00%	0,00%	20,00%	20,00%	
2.5	Blind Flange & Split Ring for Hydrotest	9,00%	22-Oct-26	21-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
2.6	Tie Rod SA 36 or Equivalent	5,00%	08-Nov-26	08-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
2.7	Hex Nut SA 192 2H	5,00%	08-Nov-26	08-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
2.8	Eye Bolt & Plug	7,00%	19-Nov-26	03-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
2.9	Gasket Flat Metal Jacketed Asbestos Fibre	7,00%	19-Nov-26	03-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
2.10	Painting Material	7,00%	19-Nov-26	03-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
2.1	MATERIAL FOR CHANNEL ASSY	40,00%	24-Aug-26	25-Nov-26	7,00%	1,76%	8,76%	7,00%	34,00%	41,00%	
2.1	Forging SA 105 for Girth Flange	22,00%	24-Aug-26	22-Nov-26	26,00%	8,00%	34,00%	26,00%	8,00%	34,00%	
2.2	Plate SA 516 Gr.70 for Channel & Partition Plate, Lifting Lug	18,00%	28-Sep-26	12-Dec-26	0,00%	0,00%	0,00%	0,00%	7,00%	7,00%	
2.3	Blind Flange for Hydrotest	12,00%	29-Oct-26	14-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
2.4	Pipe SA 106 Gr.B for Nozzle	8,00%	23-Sep-26	23-Oct-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
2.5	WNRF Flange SA 105	8,00%	16-Oct-26	15-Nov-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
2.6	Coupling & Plug SA 105	8,00%	16-Oct-26	15-Nov-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
2.7	Welding Electrode	8,00%	09-Oct-26	08-Nov-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
2.8	Stud Bolt & Nut	8,00%	16-Oct-26	15-Nov-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
2.9	Gasket	8,00%	16-Oct-26	15-Nov-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	

Prepared by,
PT Intan Prima Kalorindo

Rama Danu Fahriza
Monday, 21 September 2026

Checked by,
PT Intan Prima Kalorindo

Hadi Ramdan
Monday, 21 September 2026

Approved by,
PT. PERTAMINA PATRA NIAGA RU IV CILACAP

Name :
Date :

PENGADAAN CHANNEL ASSY 38-E-110, 12-E-522A, 14-E-201A&B, 12-E-501B 12-E-522C & TUBE BUNDLE ASSY 16-E-120C, 16-E-108, 16-E-113, 16-E-114, 19-E-107, 20-E-109A, 20-E-109B
FABRICATION WORKS

Manufacture : KALORINDO PT. INTAN PRIMA KALORINDO

Client : PERTAMINA PATRA NIAGA

Contract No. : 4500074960
Project Name : Pengadaan Channel Assy 38-E-110, 12-E-522A, 14-E-201A&B, 12-E-522C, 12-E-501B & Pengadaan Tube Bundle Assy 16-E-102C, 16-E-108, 16-E-113, 16-E-114, 19-E-107, 20-E-109A, 20-E-109B
Plant : PT. PERTAMINA PATRA NIAGA RU VI Balongan
Cut of Date : 6 21-Sep-26
Revision No. : 0

No.	Description Item	Weight Factor (%)	Schedule Plan		Plan			Actual			Remarks
			Start	Finish	Last Week	This Week	Cumulative	Last Week	This Week	Cumulative	
3	FABRICATION WORKS	32,64%	17-Oct-26	14-Feb-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.1	Tube Bundle Tag No. 16-E-113	10,00%	17-Oct-26	25-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.1.1	Baffles	38,00%	17-Oct-26	14-Nov-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.1.2	Support Baffle	9,00%	17-Nov-26	24-Nov-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.1.3	Tube Spacer	3,00%	19-Dec-26	21-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.1.4	Tie Rod	4,00%	22-Dec-26	25-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.1.7	Assembling	46,00%	20-Dec-26	23-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.1.7.1 Setting Tubesheet	12,00%	20-Dec-26	22-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.1.7.2 Setting Baffle, Support Baffle, Tie Rod & Tube Spacer	12,00%	25-Dec-26	27-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.1.7.3 Insert Tube	12,00%	14-Jan-27	16-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.1.7.4 Fit Up & Welding Seal Bars & Skid Bars	6,00%	16-Jan-27	17-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.1.7.5 Fit Up & Welding Impingement	12,00%	16-Jan-27	18-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.1.7.6 NDT	5,00%	18-Jan-27	19-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.1.7.7 Expand	29,00%	18-Jan-27	23-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.1.7.8 Pre-Hydrotest	12,00%	23-Jan-27	25-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.2	Tube Bundle Tag No. 16-E-108	11,00%	06-Nov-26	14-Feb-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.2.1	Baffles	40,00%	06-Nov-26	18-Nov-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.2.2	Support Baffle	13,00%	17-Nov-26	21-Nov-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.2.3	Tube Spacer	3,00%	19-Dec-26	20-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.2.4	Tie Rod	7,00%	22-Dec-26	24-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.2.5	Assembling	37,00%	01-Feb-27	12-Feb-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.2.5.1 Setting Tubesheet	7,00%	01-Feb-27	02-Feb-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.2.5.2 Setting Baffle, Support Baffle, Tie Rod & Tube Spacer	13,00%	02-Feb-27	04-Feb-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.2.5.3 Insert Tube	13,00%	04-Feb-27	06-Feb-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.2.5.4 Fit Up & Welding Seal Bars & Skid Bars	7,00%	06-Feb-27	07-Feb-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.2.5.5 Fit Up & Welding Impingement	13,00%	06-Feb-27	08-Feb-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.2.5.6 NDT	7,00%	08-Feb-27	09-Feb-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.2.5.7 Expand	27,00%	08-Feb-27	12-Feb-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.2.5.8 Pre-Hydrotest	13,00%	12-Feb-27	14-Feb-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.3	Tube Bundle Tag No. 19-E-107	5,00%	19-Nov-26	04-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.3.1	Baffles	29,00%	19-Nov-26	29-Nov-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.3.2	Support Baffle	12,00%	28-Nov-26	02-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.3.3	Tube Spacer	6,00%	19-Dec-26	21-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.3.4	Tie Rod	6,00%	22-Dec-26	24-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.3.5	Sliding Plate	9,00%	02-Dec-26	05-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.3.6	Impingement Plate	6,00%	02-Dec-26	04-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.3.7	Assembling	32,00%	22-Dec-26	02-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.3.7.1 Setting Stationary Tubesheet	13,00%	22-Dec-26	24-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.3.7.2 Setting Baffle, Support Baffle, Tie Rod & Tube Spacer	13,00%	24-Dec-26	26-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.3.7.3 Setting Floating Tubesheet	6,00%	26-Dec-26	27-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.3.7.4 Insert Tube	6,00%	27-Dec-26	28-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.3.7.5 Expand	19,00%	28-Dec-26	31-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.3.7.6 Fit Up & Welding Seal Bars & Skid Bars	12,00%	30-Dec-26	01-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.3.7.7 Fit Up & Welding Impingement	12,00%	30-Dec-26	01-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.3.7.8 NDT	6,00%	01-Jan-27	02-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.3.7.9 Pre-Hydrotest	13,00%	02-Jan-27	04-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.4	Tube Bundle Tag No. 16-E-102C	5,00%	22-Nov-26	06-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.4.1	Baffles #1 ~ #5	43,00%	22-Nov-26	12-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.4.2	Support Baffle	6,00%	11-Dec-26	14-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.4.3	Tube Spacer	4,00%	19-Dec-26	21-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.4.4	Tie Rod	4,00%	22-Dec-26	24-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.4.5	Skid Bars	6,00%	14-Dec-26	17-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.4.6	Seal Bars	6,00%	17-Dec-26	20-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.4.7	Impingement Plate	4,00%	14-Dec-26	16-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.4.8	Assembling	27,00%	23-Dec-26	04-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.4.8.1 Setting Stationary Tubesheet	12,00%	23-Dec-26	25-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.4.8.2 Setting Baffle, Support Baffle, Tie Rod & Tube Spacer	6,00%	25-Dec-26	26-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.4.8.3 Setting Floating Tubesheet	6,00%	26-Dec-26	27-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.4.8.4 Insert Tube	6,00%	27-Dec-26	28-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.4.8.5 Expand	28,00%	28-Dec-26	02-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.4.8.6 Fit Up & Welding Seal Bars & Skid Bars	12,00%	01-Jan-27	03-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.4.8.7 Fit Up & Welding Impingement	12,00%	01-Jan-27	03-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.4.8.8 NDT	6,00%	03-Jan-27	04-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.4.8.9 Pre-Hydrotest	12,00%	04-Jan-27	06-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	

PENGADAAN CHANNEL ASSY 38-E-110, 12-E-522A, 14-E-201A&B, 12-E-501B 12-E-522C & TUBE BUNDLE ASSY 16-E-120C, 16-E-108, 16-E-113, 16-E-114, 19-E-107, 20-E-109A, 20-E-109B
FABRICATION WORKS

Manufacture : KALORINDO PT. INTAN PRIMA KALORINDO

Client : PERTAMINA PATRA NIAGA

Contract No.	:	4500074960
Project Name	:	Pengadaan Channel Assy 38-E-110, 12-E-522A, 14-E-201A&B, 12-E-522C, 12-E-501B & Pengadaan Tube Bundle Assy 16-E-102C, 16-E-108, 16-E-113, 16-E-114, 19-E-107, 20-E-109A, 20-E-109B
Plant	:	PT. PERTAMINA PATRA NIAGA RU VI Balongan
Cut of Date	:	6 21-Sep-26
Revision No.	:	0

No.	Description Item	Weight Factor (%)	Schedule Plan		Plan			Actual			Remarks
			Start	Finish	Last Week	This Week	Cumulative	Last Week	This Week	Cumulative	

Prepared by,
PT Intan Prima Kalorindo

Rama Danu Fahriza
Monday, 21 September 2026

Checked by,
PT Intan Prima Kalorindo

Hadi Ramdan
Monday, 21 September 2026

Approved by,
PT. PERTAMINA PATRA NIAGA RU VI BALONGAN

Name :
Date :

PENGADAAN CHANNEL ASSY 38-E-110, 12-E-522A, 14-E-201A&B, 12-E-501B 12-E-522C & TUBE BUNDLE ASSY 16-E-120C, 16-E-108, 16-E-113, 16-E-114, 19-E-107, 20-E-109A, 20-E-109B
FABRICATION WORKS

Manufacture : KALORINDO PT. INTAN PRIMA KALORINDO

Client : PERTAMINA PATRA NIAGA

Contract No. : 4500074960
Project Name : Pengadaan Channel Assy 38-E-110, 12-E-522A, 14-E-201A&B, 12-E-522C, 12-E-501B & Pengadaan Tube Bundle Assy 16-E-102C, 16-E-108, 16-E-113, 16-E-114, 19-E-107, 20-E-109A, 20-E-109B
Plant : PT. PERTAMINA PATRA NIAGA RU VI Balongan
Cut of Date : 6 21-Sep-26
Revision No. : 0

No.	Description Item	Weight Factor (%)	Schedule Plan		Plan			Actual			Remarks
			Start	Finish	Last Week	This Week	Cumulative	Last Week	This Week	Cumulative	
3.5	Tube Bundle Tag No. 16-E-114	8,00%	07-Nov-26	24-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.5.1	Baffles Assy	52,00%	07-Nov-26	18-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.5.2	Support Baffle	4,00%	13-Dec-26	16-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.5.3	Tube Spacer	3,00%	19-Dec-26	21-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.5.4	Tie Rod	4,00%	22-Dec-26	25-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.5.5	Assembling	37,00%	24-Dec-26	22-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.5.5.1 Setting Tubesheet	11,00%	24-Dec-26	26-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.5.5.2 Setting Baffle, Support Baffle, Tie Rod & Tube Spacer	22,00%	26-Dec-26	30-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.5.5.3 Insert Tube	11,00%	14-Jan-26	16-Jan-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.5.5.4 Fit Up & Welding Seal Bars & Skid Bars	6,00%	16-Jan-26	17-Jan-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.5.5.5 Fit Up & Welding Impingement	11,00%	16-Jan-26	18-Jan-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.5.5.6 NDT	6,00%	18-Jan-26	19-Jan-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.5.5.7 Expand	22,00%	18-Jan-27	22-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.5.5.8 Pre-Hydrotest	11,00%	22-Jan-27	24-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.6	Tube Bundle Tag No. 20-E-109A	3,00%	14-Dec-26	12-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.6.1	Baffles	31,00%	14-Dec-26	28-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.6.2	Support Baffle	7,00%	27-Dec-26	30-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.6.3	Tube Spacer	4,00%	19-Dec-26	21-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.6.4	Tie Rod	4,00%	22-Dec-26	24-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.6.5	Skid Bars	7,00%	30-Dec-26	02-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.6.6	Seal Bars	7,00%	02-Jan-27	05-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.6.7	Impingement Plate	4,00%	30-Dec-26	01-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.6.8	Assembling	36,00%	25-Dec-26	10-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.6.8.1 Setting Stationary Tubesheet	11,00%	25-Dec-26	27-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.6.8.2 Setting Baffle, Support Baffle, Tie Rod & Tube Spacer	6,00%	30-Dec-26	31-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.6.8.3 Setting Floating Tubesheet	6,00%	31-Dec-26	01-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.6.8.4 Insert Tube	11,00%	01-Jan-27	03-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.6.8.5 Expand	27,00%	03-Jan-27	08-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.6.8.6 Fit Up & Welding Seal Bars & Skid Bars	11,00%	07-Jan-27	09-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.6.8.7 Fit Up & Welding Impingement	11,00%	07-Jan-27	09-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.6.8.8 NDT	6,00%	09-Jan-27	10-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.6.8.9 Pre-Hydrotest	11,00%	10-Jan-27	12-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.7	Tube Bundle Tag No. 20-E-109B	4,00%	19-Dec-26	26-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.7.1	Baffles	35,00%	28-Dec-26	12-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.7.2	Support Baffle	7,00%	11-Jan-27	14-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.7.3	Tube Spacer	5,00%	19-Dec-26	21-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.7.4	Tie Rod	5,00%	22-Dec-26	24-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.7.5	Skid Bars	7,00%	14-Jan-27	17-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.7.6	Seal Bars	7,00%	17-Jan-27	20-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.7.7	Impingement Plate	5,00%	14-Jan-27	16-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.7.8	Assembling	29,00%	12-Jan-27	24-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.7.8.1 Setting Stationary Tubesheet	12,00%	12-Jan-27	14-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.7.8.2 Setting Baffle, Support Baffle, Tie Rod & Tube Spacer	6,00%	14-Jan-27	15-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.7.8.3 Setting Floating Tubesheet	6,00%	15-Jan-27	16-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.7.8.4 Insert Tube	12,00%	16-Jan-27	18-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.7.8.5 Expand	23,00%	18-Jan-27	22-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.7.8.6 Fit Up & Welding Seal Bars & Skid Bars	12,00%	21-Jan-27	23-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.7.8.7 Fit Up & Welding Impingement	12,00%	21-Jan-27	23-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.7.8.8 NDT	6,00%	23-Jan-27	24-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.7.8.9 Pre-Hydrotest	11,00%	24-Jan-27	26-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	

Prepared by,
PT Intan Prima Kalorindo

Rama Danu Fahriza
Monday, 21 September 2026

Checked by,
PT Intan Prima Kalorindo

Hadi Ramdan
Monday, 21 September 2026

Approved by,
PT. PERTAMINA PATRA NIAGA RU VI BALONGAN

Name :
Date :

PENGADAAN CHANNEL ASSY 38-E-110, 12-E-522A, 14-E-201A&B, 12-E-501B 12-E-522C & TUBE BUNDLE ASSY 16-E-120C, 16-E-108, 16-E-113, 16-E-114, 19-E-107, 20-E-109A, 20-E-109B
FABRICATION WORKS

Manufacture : KALORINDO PT. INTAN PRIMA KALORINDO

Client : PERTAMINA PATRA NIAGA

Contract No. : 4500074960
Project Name : Pengadaan Channel Assy 38-E-110, 12-E-522A, 14-E-201A&B, 12-E-522C, 12-E-501B & Pengadaan Tube Bundle Assy 16-E-102C, 16-E-108, 16-E-113, 16-E-114, 19-E-107, 20-E-109A, 20-E-109B
Plant : PT. PERTAMINA PATRA NIAGA RU VI Balongan
Cut of Date : 6 21-Sep-26
Revision No. : 0

No.	Description Item	Weight Factor (%)	Schedule Plan		Plan			Actual			Remarks
			Start	Finish	Last Week	This Week	Cumulative	Last Week	This Week	Cumulative	
3.8	**Channel Assy 14-E-201A**	10,00%	28-Oct-26	20-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.8.1	**Channel Shell**	23,00%	28-Oct-26	13-Nov-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.8.2	**Cover Channel**	6,00%	25-Nov-26	29-Nov-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.8.3	**Reinforced Pad**	15,00%	30-Oct-26	09-Nov-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.8.4	**Pass Partition Plate**	4,00%	07-Nov-26	10-Nov-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.8.5	**Lifting Lug**	3,00%	08-Nov-26	10-Nov-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.8.6	**Nozzle Flange Assy**	9,00%	27-Nov-26	03-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.8.7	**Assembly Channel Assy**	40,00%	25-Nov-26	22-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.8.7.1 Fit Up & Welding Channel Shell to Flange	17,00%	25-Nov-26	30-Nov-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.8.7.2 NDT	7,00%	30-Nov-26	02-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.8.7.3 Cutting & Bevelling Nozzle Holes	7,00%	02-Dec-26	04-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.8.7.4 Fit Up Nozzle Flange & Reinforced Pad	3,00%	04-Dec-26	05-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.8.7.5 Welding Nozzle Flange	11,00%	05-Dec-26	08-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.8.7.6 NDT	3,00%	08-Dec-26	09-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.8.7.7 Welding Reinforced Pad	11,00%	09-Dec-26	12-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.8.7.8 Fit up & Welding Partition Plate	11,00%	12-Dec-26	15-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.8.7.9 Fit Up & Welding Lifting Lug	3,00%	15-Dec-26	16-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.8.7.10 NDT	3,00%	16-Dec-26	17-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.8.7.11 PWHT	7,00%	17-Dec-26	19-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.8.7.12 NDT	3,00%	19-Dec-26	20-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.8.7.13 Machining Partition Plate	7,00%	20-Dec-26	22-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.8.7.14 Pre-Hydrotest	7,00%	22-Dec-26	24-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.9	**Channel Assy 14-E-201B**	8,00%	28-Oct-26	31-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.9.1	**Channel Shell**	23,00%	28-Oct-26	13-Nov-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.9.2	**Cover Channel**	6,00%	29-Nov-26	03-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.9.3	**Reinforced Pad**	15,00%	30-Oct-26	09-Nov-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.9.4	**Pass Partition Plate**	4,00%	07-Nov-26	10-Nov-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.9.5	**Lifting Lug**	3,00%	08-Nov-26	10-Nov-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.9.6	**Nozzle Flange Assy**	9,00%	27-Nov-26	03-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.9.7	**Assembly Channel Assy**	40,00%	01-Dec-26	29-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.9.7.1 Fit Up & Welding Channel Shell to Flange	17,00%	01-Dec-26	07-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.9.7.2 NDT	7,00%	07-Dec-26	09-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.9.7.3 Cutting & Bevelling Nozzle Holes	7,00%	09-Dec-26	11-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.9.7.4 Fit Up Nozzle Flange & Reinforced Pad	3,00%	11-Dec-26	12-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.9.7.5 Welding Nozzle Flange	11,00%	12-Dec-26	15-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.9.7.6 NDT	3,00%	15-Dec-26	16-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.9.7.7 Welding Reinforced Pad	11,00%	16-Dec-26	19-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.9.7.8 Fit up & Welding Partition Plate	11,00%	19-Dec-26	22-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.9.7.9 Fit Up & Welding Lifting Lug	3,00%	22-Dec-26	23-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.9.7.10 NDT	3,00%	23-Dec-26	24-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.9.7.11 PWHT	7,00%	24-Dec-26	26-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.9.7.12 NDT	3,00%	26-Dec-26	27-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.9.7.13 Machining Partition Plate	7,00%	27-Dec-26	29-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.9.7.14 Pre-Hydrotest	7,00%	29-Dec-26	31-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.10	**Channel Assy 38-E-110**	8,00%	28-Oct-26	02-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.10.1	**Channel Shell**	25,00%	28-Oct-26	14-Nov-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.10.2	**Channel Head**	25,00%	31-Oct-26	17-Nov-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.10.3	**Pass Partition Plate**	4,00%	08-Nov-26	11-Nov-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.10.4	**Lifting Lug**	3,00%	09-Nov-26	11-Nov-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.10.5	**Nozzle Flange Assy**	9,00%	27-Nov-26	03-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.10.6	**Assembly Channel Assy**	34,00%	07-Dec-26	31-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.10.6.1 Fit Up Channel Shell to Flange & Channel Head	9,00%	07-Dec-26	09-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.10.6.2 Welding Channel Shell to Flange & Channel Head	25,00%	09-Dec-26	15-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.10.6.3 NDT	9,00%	15-Dec-26	17-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.10.6.4 Cutting & Bevelling Nozzle Holes	9,00%	17-Dec-26	19-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.10.6.5 Fit Up Nozzle Flange	4,00%	19-Dec-26	20-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.10.6.6 Welding Nozzle Flange	9,00%	20-Dec-26	22-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.10.6.7 Fit up & Welding Partition Plate	9,00%	22-Dec-26	24-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.10.6.8 Fit Up & Welding Lifting Lug	4,00%	24-Dec-26	25-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.10.6.9 NDT	4,00%	25-Dec-26	26-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.10.6.10 Machining Partition Plate	9,00%	29-Dec-26	31-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.10.6.11 Pre-Hydrotest	9,00%	31-Dec-26	02-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	

Prepared by, Checked by, Approved by,

Manufacture : Client :

PENGADAAN CHANNEL ASSY 38-E-110, 12-E-522A, 14-E-201A&B, 12-E-501B 12-E-522C & TUBE BUNDLE ASSY 16-E-120C, 16-E-108, 16-E-113, 16-E-114, 19-E-107, 20-E-109A, 20-E-109B
FABRICATION WORKS

Contract No.	:	4500074960
Project Name	:	Pengadaan Channel Assy 38-E-110, 12-E-522A, 14-E-201A&B, 12-E-522C, 12-E-501B & Pengadaan Tube Bundle Assy 16-E-102C, 16-E-108, 16-E-113, 16-E-114, 19-E-107, 20-E-109A, 20-E-109B
Plant	:	PT. PERTAMINA PATRA NIAGA RU VI Balongan
Cut of Date	:	6 21-Sep-26
Revision No.	:	0

No.	Description Item	Weight Factor (%)	Schedule Plan		Plan			Actual			Remarks
			Start	Finish	Last Week	This Week	Cumulative	Last Week	This Week	Cumulative	

PT Intan Prima Kalorindo	PT Intan Prima Kalorindo	PT. PERTAMINA PATRA NIAGA RU VI BALONGAN
Rama Danu Fahriza	Hadi Ramdan	Name :
Monday, 21 September 2026	Monday, 21 September 2026	Date :

PENGADAAN CHANNEL ASSY 38-E-110, 12-E-522A, 14-E-201A&B, 12-E-501B 12-E-522C & TUBE BUNDLE ASSY 16-E-120C, 16-E-108, 16-E-113, 16-E-114, 19-E-107, 20-E-109A, 20-E-109B
FABRICATION WORKS

Manufacture : KALORINDO PT. INTAN PRIMA KALORINDO

Client : PERTAMINA PATRA NIAGA

Contract No. : 4500074960
Project Name : Pengadaan Channel Assy 38-E-110, 12-E-522A, 14-E-201A&B, 12-E-522C, 12-E-501B & Pengadaan Tube Bundle Assy 16-E-102C, 16-E-108, 16-E-113, 16-E-114, 19-E-107, 20-E-109A, 20-E-109B
Plant : PT. PERTAMINA PATRA NIAGA RU VI Balongan
Cut of Date : 6 21-Sep-26
Revision No. : 0

No.	Description Item	Weight Factor (%)	Schedule Plan		Plan			Actual			Remarks
			Start	Finish	Last Week	This Week	Cumulative	Last Week	This Week	Cumulative	
3.11	Channel Assy 12-E-522A	9,00%	28-Oct-26	10-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.11.1	Channel Shell	24,00%	28-Oct-26	13-Nov-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.11.2	Cover Channel	6,00%	28-Nov-26	02-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.11.3	Reinforced Pad	15,00%	30-Oct-26	09-Nov-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.11.4	Pass Partition Plate	5,00%	07-Nov-26	10-Nov-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.11.5	Lifting Lug	4,00%	08-Nov-26	10-Nov-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.11.6	Nozzle Flange Assy	9,00%	27-Nov-26	03-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.11.7	Assembly Channel Assy	37,00%	15-Dec-26	08-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.11.7.1 Fit Up & Welding Channel Shell to Flange	14,00%	15-Dec-26	19-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.11.7.2 NDT	8,00%	19-Dec-26	21-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.11.7.3 Cutting & Bevelling Nozzle Holes	8,00%	21-Dec-26	23-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.11.7.4 Fit Up Nozzle Flange & Reinforced Pad	14,00%	23-Dec-26	27-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.11.7.5 Welding Nozzle Flange	8,00%	27-Dec-26	29-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.11.7.6 NDT	4,00%	29-Dec-26	30-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.11.7.7 Welding Reinforced Pad	12,00%	30-Dec-26	02-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.11.7.8 Fit up & Welding Partition Plate	8,00%	02-Jan-27	04-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.11.7.9 Fit Up & Welding Lifting Lug	4,00%	04-Jan-27	05-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.11.7.10 NDT	4,00%	05-Jan-27	06-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.11.7.11 Machining Partition Plate	8,00%	06-Jan-27	08-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.11.7.12 Pre-Hydrotest	8,00%	08-Jan-27	10-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.12	Channel Assy 12-E-522C	9,00%	28-Oct-26	12-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.12.1	Channel Shell	25,00%	28-Oct-26	13-Nov-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.12.2	Cover Channel	6,00%	30-Nov-26	04-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.12.3	Reinforced Pad	15,00%	30-Oct-26	09-Nov-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.12.4	Pass Partition Plate	5,00%	07-Nov-26	10-Nov-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.12.5	Lifting Lug	3,00%	08-Nov-26	10-Nov-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.12.6	Nozzle Flange Assy	9,00%	27-Nov-26	03-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.12.7	Assembly Channel Assy	37,00%	19-Dec-26	10-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.12.7.1 Fit Up & Welding Channel Shell to Flange	14,00%	19-Dec-26	23-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.12.7.2 NDT	8,00%	23-Dec-26	25-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.12.7.3 Cutting & Bevelling Nozzle Holes	8,00%	25-Dec-26	27-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.12.7.4 Fit Up Nozzle Flange & Reinforced Pad	14,00%	27-Dec-26	28-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.12.7.5 Welding Nozzle Flange	8,00%	28-Dec-26	30-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.12.7.6 NDT	4,00%	30-Dec-26	31-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.12.7.7 Welding Reinforced Pad	12,00%	31-Dec-26	03-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.12.7.8 Fit up & Welding Partition Plate	8,00%	03-Jan-27	05-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.12.7.9 Fit Up & Welding Lifting Lug	4,00%	05-Jan-27	06-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.12.7.10 NDT	4,00%	06-Jan-27	07-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.12.7.11 Machining Partition Plate	8,00%	08-Jan-27	10-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.12.7.12 Pre-Hydrotest	8,00%	10-Jan-27	12-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.13	Channel Assy 12-E-501B	10,00%	28-Oct-26	20-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.13.1	Channel Shell	24,00%	28-Oct-26	13-Nov-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.13.2	Cover Channel	7,00%	02-Dec-26	06-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.13.3	Reinforced Pad	15,00%	30-Oct-26	09-Nov-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.13.4	Pass Partition Plate	5,00%	07-Nov-26	10-Nov-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.13.5	Lifting Lug	3,00%	08-Nov-26	10-Nov-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.13.6	Nozzle Flange Assy	9,00%	27-Nov-26	03-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
3.13.7	Assembly Channel Assy	37,00%	23-Dec-26	18-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.13.7.1 Fit Up & Welding Channel Shell to Flange	12,00%	23-Dec-26	29-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.13.7.2 NDT	3,00%	29-Dec-26	31-Dec-26	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.13.7.3 Cutting & Bevelling Nozzle Holes	4,00%	31-Dec-26	02-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.13.7.4 Fit Up Nozzle Flange & Reinforced Pad	12,00%	02-Jan-27	03-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.13.7.5 Welding Nozzle Flange	14,00%	03-Jan-27	05-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.13.7.6 NDT	8,00%	05-Jan-27	06-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.13.7.7 Welding Reinforced Pad	8,00%	06-Jan-27	09-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.13.7.8 Fit up & Welding Partition Plate	12,00%	09-Jan-27	12-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.13.7.9 Fit Up & Welding Lifting Lug	8,00%	12-Jan-27	13-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.13.7.10 NDT	3,00%	13-Jan-27	14-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.13.7.11 PWHT	4,00%	14-Jan-27	16-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.13.7.12 Machining Partition Plate	6,00%	16-Jan-27	18-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
	3.13.7.13 Pre-Hydrotest	6,00%	18-Jan-27	20-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	

Prepared by,
PT Intan Prima Kalorindo

Checked by,
PT Intan Prima Kalorindo

Approved by,
PT. PERTAMINA PATRA NIAGA RU VI BALONGAN

Manufacture : Client :

PENGADAAN CHANNEL ASSY 38-E-110, 12-E-522A, 14-E-201A&B, 12-E-501B 12-E-522C & TUBE BUNDLE ASSY 16-E-120C, 16-E-108, 16-E-113, 16-E-114, 19-E-107, 20-E-109A, 20-E-109B
FABRICATION WORKS

KALORINDO
PT. INTAN PRIMA KALORINDO

PERTAMINA
PATRA NIAGA

Contract No.	:	**4500074960**
Project Name	:	**Pengadaan Channel Assy 38-E-110, 12-E-522A, 14-E-201A&B, 12-E-522C, 12-E-501B & Pengadaan Tube Bundle Assy 16-E-102C, 16-E-108, 16-E-113, 16-E-114, 19-E-107, 20-E-109A, 20-E-109B**
Plant	:	**PT. PERTAMINA PATRA NIAGA RU VI Balongan**
Cut of Date	:	**6** **21-Sep-26**
Revision No.	:	**0**

No.	Description Item	Weight Factor (%)	Schedule Plan		Plan			Actual			Remarks
			Start	Finish	Last Week	This Week	Cumulative	Last Week	This Week	Cumulative	

Rama Danu Fahriza
Monday, 21 September 2026

Hadi Ramdan
Monday, 21 September 2026

Name :
Date :

PENGADAAN CHANNEL ASSY 38-E-110, 12-E-522A, 14-E-201A&B, 12-E-501B 12-E-522C & TUBE BUNDLE ASSY 16-E-120C, 16-E-108, 16-E-113, 16-E-114, 19-E-107, 20-E-109A, 20-E-109B
TESTING, PACKAGING & DELIVERY WORKS

Manufacture : KALORINDO — PT. INTAN PRIMA KALORINDO

Client : PERTAMINA PATRA NIAGA

Contract No. : 4500074960
Project Name : Pengadaan Channel Assy 38-E-110, 12-E-522A, 14-E-201A&B, 12-E-522C, 12-E-501B & Pengadaan Tube Bundle Assy 16-E-102C, 16-E-108, 16-E-113, 16-E-114, 19-E-107, 20-E-109A, 20-E-109B
Plant : PT. PERTAMINA PATRA NIAGA RU VI Balongan
Cut of Date : 6 21-Sep-26
Revision No. : 0

No.	Description Item	Weight Factor (%)	Schedule Plan		Plan			Actual			Remarks
			Start	Finish	Last Week	This Week	Cumulative	Last Week	This Week	Cumulative	
4	TESTING	0,52%	31-Dec-26	02-Feb-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
2.1	TESTING FOR TUBE BUNDLE	50,00%	25-Jan-27	02-Feb-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
4.1	Batch 1 (16-E-113,16-E-108,19-E-107,16-E-102C,16-E-114)	50,00%	25-Jan-27	28-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
4.2	Batch 2 (20-E-109A & 20-E-109B)	50,00%	31-Jan-27	02-Feb-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
2.1	TESTING FOR CHANNEL ASSY	50,00%	31-Dec-26	22-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
4.1	Batch 1 (14-E-201A & 14-E-201B)	50,00%	31-Dec-26	02-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
4.2	Batch 2 (38-E-110, 12-E-522A, 12-E-522C, 12-E-501B)	50,00%	20-Jan-27	22-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
5	FINISHING & PACKAGING	2,09%	09-Jan-27	04-Feb-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
2.1	PACKAGING FOR TUBE BUNDLE	50,00%	09-Jan-27	04-Feb-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
5.1	Batch 1 (16-E-113,16-E-108,19-E-107,16-E-102C,16-E-114)	50,00%	28-Jan-27	31-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
5.2	Batch 2 (20-E-109A & 20-E-109B)	50,00%	02-Feb-27	04-Feb-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
2.1	PACKAGING FOR CHANNEL ASSY	50,00%	09-Jan-27	04-Feb-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
5.1	Batch 1 (14-E-201A & 14-E-201B)	50,00%	09-Jan-27	11-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
5.2	Batch 2 (38-E-110, 12-E-522A, 12-E-522C, 12-E-501B)	50,00%	01-Feb-27	04-Feb-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
6	DELIVERY	0,52%	11-Jan-27	16-Feb-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
2.1	DELIVERY FOR TUBE BUNDLE	50,00%	31-Jan-27	06-Feb-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
5.1	Batch 1 (16-E-113,16-E-108,19-E-107,16-E-102C,16-E-114)	50,00%	31-Jan-27	02-Feb-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
5.2	Batch 2 (20-E-109A & 20-E-109B)	50,00%	04-Feb-27	06-Feb-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
2.1	DELIVERY FOR CHANNEL	50,00%	11-Jan-27	16-Feb-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
5.1	Batch 1 (14-E-201A & 14-E-201B)	50,00%	11-Jan-27	13-Jan-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	
5.2	Batch 2 (38-E-110, 12-E-522A, 12-E-522C, 12-E-501B)	50,00%	14-Feb-27	16-Feb-27	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	

Prepared by,
PT Intan Prima Kalorindo

Rama Danu Fahriza
Monday, 21 September 2026

Checked by,
PT Intan Prima Kalorindo

Hadi Ramdan
Monday, 21 September 2026

Approved by,
PT. PERTAMINA PATRA NIAGA RU IV CILACAP

Name :
Date :

PENGADAAN CHANNEL ASSY 38-E-110, 12-E-522A, 14-E-201A&B, 12-E-501B 12-E-522C & TUBE BUNDLE ASSY 16-E-120C, 16-E-108, 16-E-113, 16-E-114, 19-E-107, 20-E-109A, 20-E-109B
DOCUMENTATION WORKS

Manufacture : KALORINDO PT. INTAN PRIMA KALORINDO

Client : PERTAMINA PATRA NIAGA

Contract No.	:	4500074960
Project Name	:	Pengadaan Channel Assy 38-E-110, 12-E-522A, 14-E-201A&B, 12-E-522C, 12-E-501B & Pengadaan Tube Bundle Assy 16-E-102C, 16-E-108, 16-E-113, 16-E-114, 19-E-107, 20-E-109A, 20-E-109B
Plant	:	PT. PERTAMINA PATRA NIAGA RU VI Balongan
Cut of Date	:	6 21-Sep-26
Revision No.	:	0

Prepared by,	Checked by,	Approved by,
PT Intan Prima Kalorindo	PT Intan Prima Kalorindo	PT. PERTAMINA PATRA NIAGA RU IV CILACAP
Rama Danu Fahriza	Hadi Ramdan	Name :
Monday, 21 September 2026	Monday, 21 September 2026	Date :
